

Mid-term review, 12 December 2013, Brussels




SeaDataNet

*PAN-EUROPEAN INFRASTRUCTURE
FOR OCEAN & MARINE DATA
MANAGEMENT*

DELIVERABLES REVIEW


66 Contractual deliverables – until Month 26

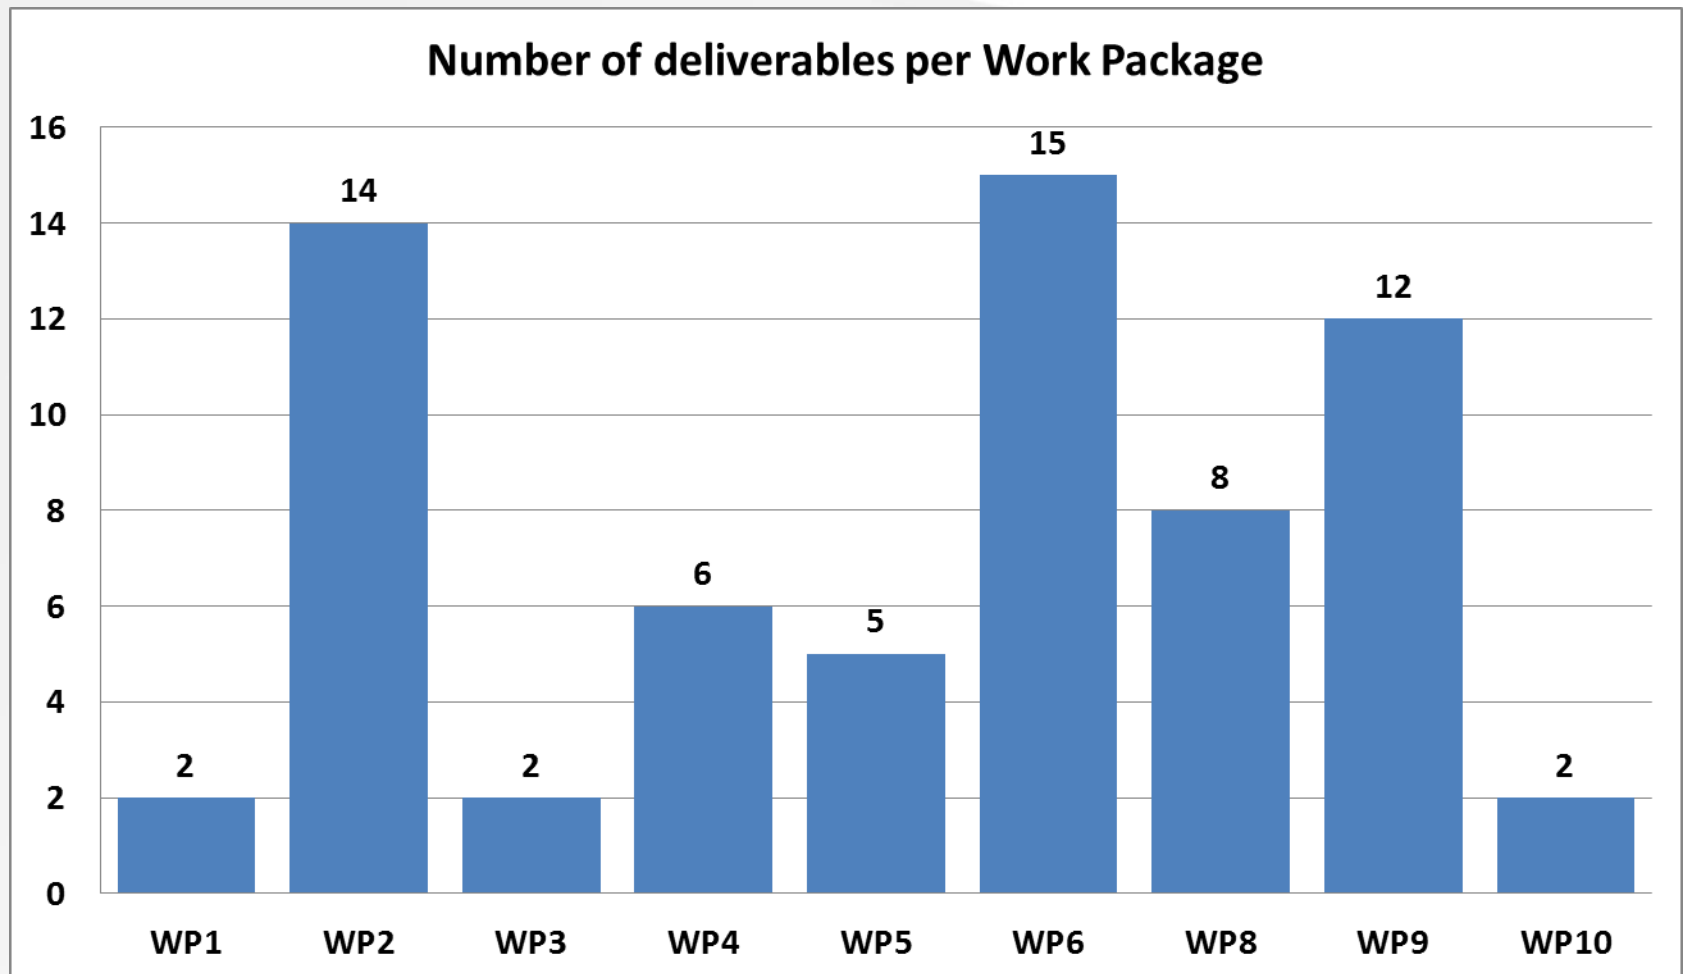

Deliverables status

- 64 among 66 have been delivered

	Nb	%	Mean delay
Delivered on time	19	29%	
Delivered with a delay < 6M	28	42%	2.68 M
Delivered with a delay > 6M	17	26%	11.12 M
Postponed to next period	2	3%	
Total	66		

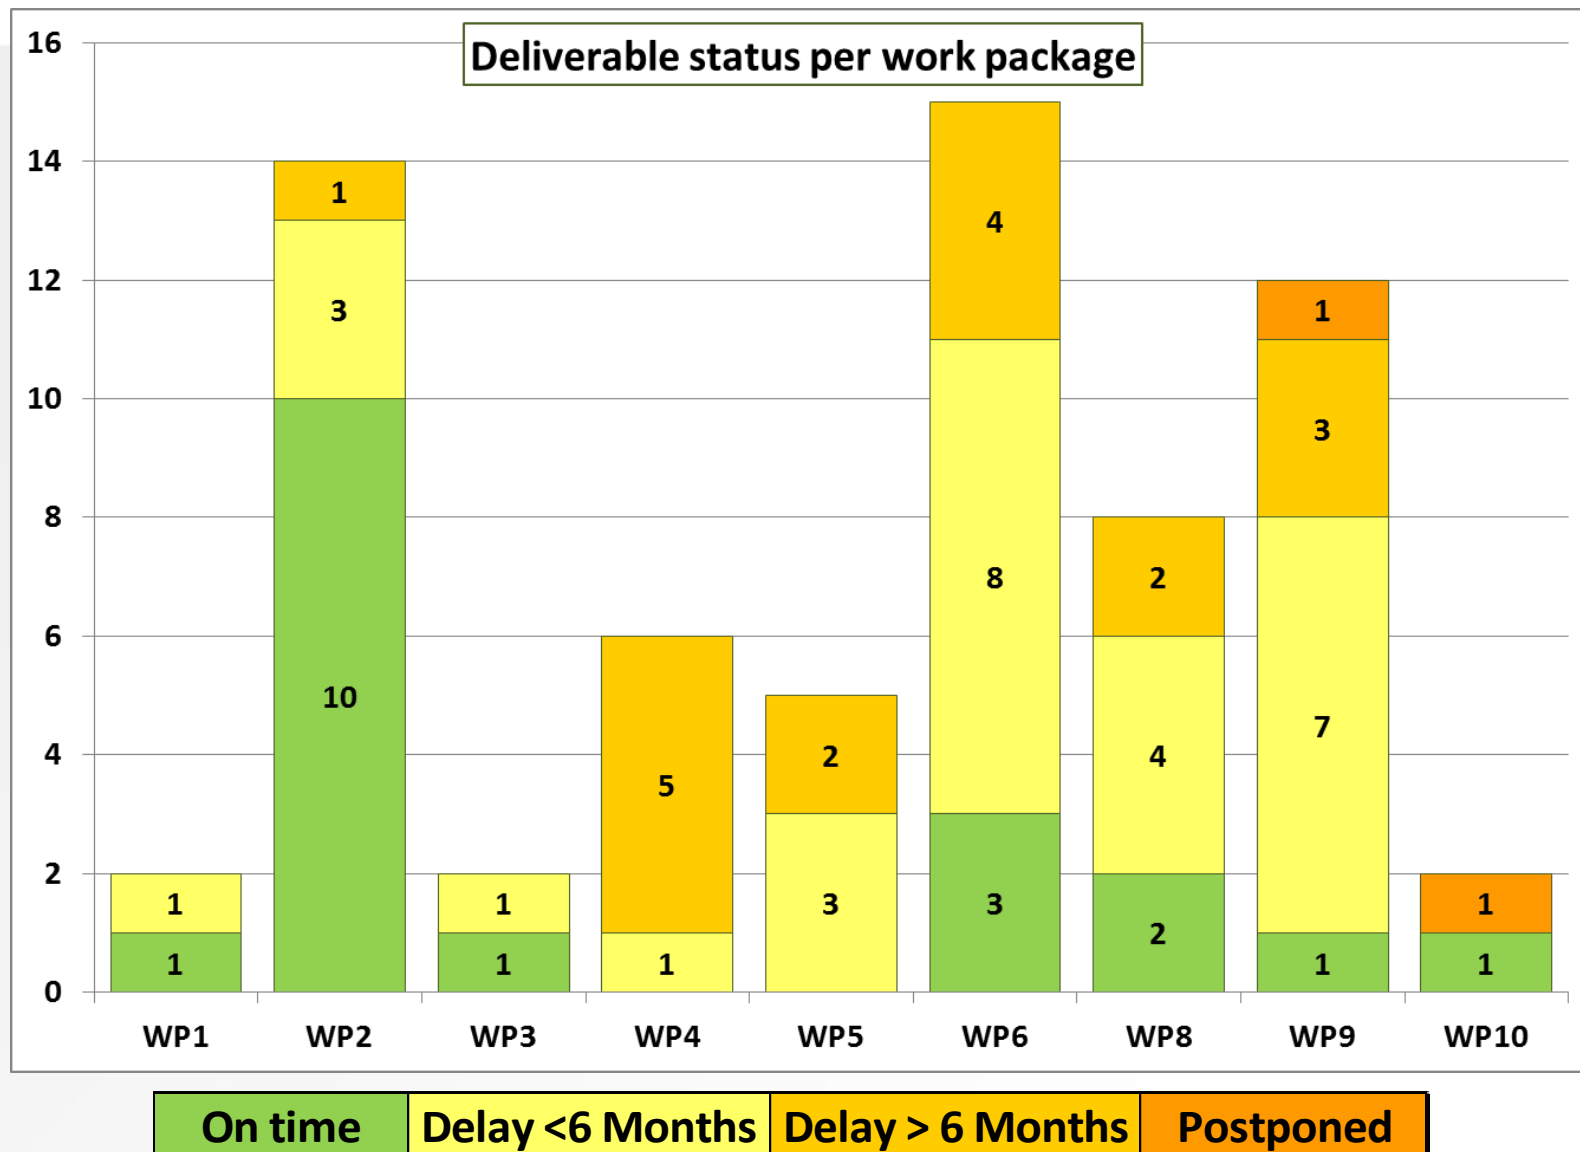

Milestones

Milestone	N°	Contractual Delivery month	Actual or planned Delivery month	Leader
Kick-off meeting	1	2	1	IFREMER
New SeaDataNet data centres connected to operational CDI services	2	6	22	MARIS
1 st training workshop	3	10	10	MUMM
End of 1 st innovation cycle – 1 st major upgrade of SDN infrastructure ready	4	18	26	MARIS
Metadata interoperability with INSPIRE portal and global portals (GEOSS, IODE/ODP)	5	18	17	RIHMI-WDC
IMDIS 2013 conference	6	22	24	IFREMER ENEA, OGS
1 st release of the aggregated data sets products	7	24	27	INGV
Machine to machine interface ready for regulated metadata and data delivery to MyOcean, WISE Marine	8	24	28	MARIS

Conclusions

- 71% have been delivered on time or with a mean short delay of 2.6 months
- Among 66 deliverables only 2 are postponed to the next period
